📅 Project Planning Template

FlightFinder - Complete Project Plan

Duration: 7 Weeks | Team Size: 6 Members

---

1. Project Overview

Attribute	Details
Project Name	FlightFinder - Flight Booking Application
Project Type	Full-Stack Web Application (MERN Stack)
Start Date	Week 1, 2026
Target Launch	Week 7, 2026
Total Duration	7 Weeks (49 Days)
Project Manager	[Name]
Budget	[Amount]

2. Project Timeline - Gantt Chart

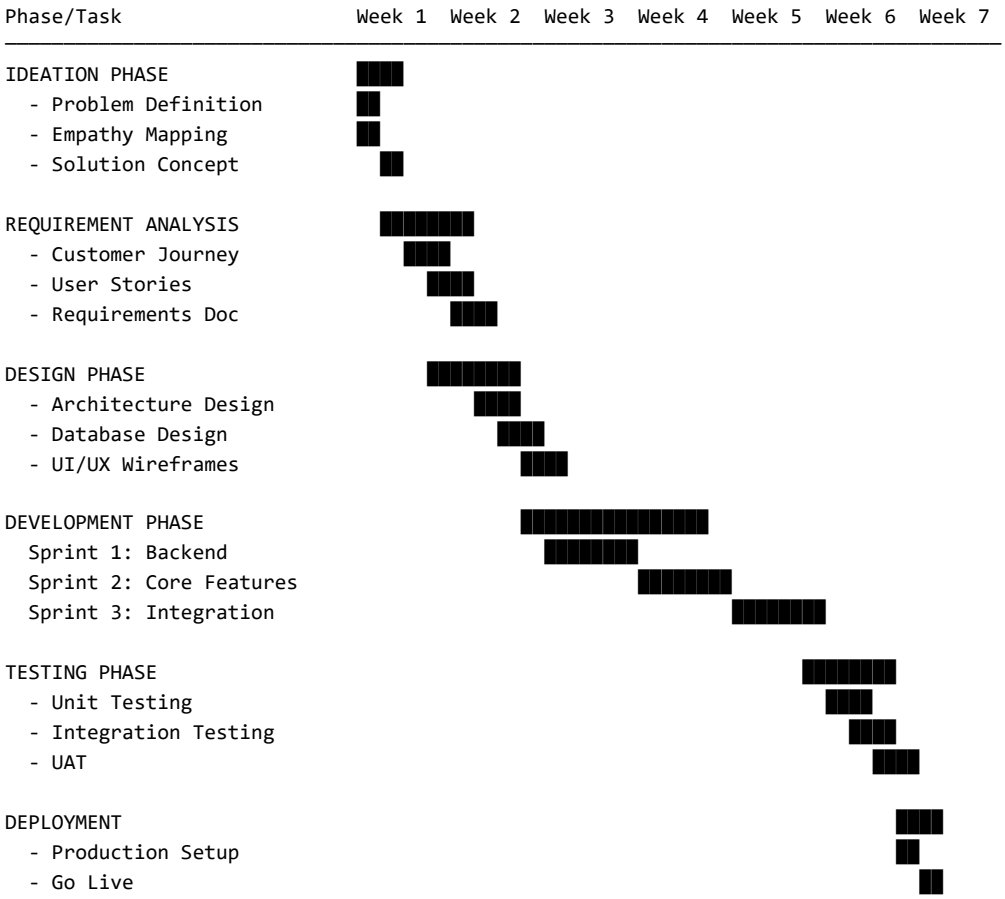

3. Phase-wise Breakdown

Phase 1: Ideation (Week 1) COMPLETE

Task	Duration	Owner	Status
Problem identification and analysis	2 days	PM + Team	✅ Done
Create empathy map canvas	1 day	Designer	✅ Done
Define problem statement	1 day	PM	✅ Done
Solution brainstorming	1 day	Team	✅ Done

Phase 2: Requirement Analysis (Week 1-2) COMPLETE

Task	Duration	Owner	Status
Customer journey mapping	2 days	Designer	✅ Done
Create user stories (12+)	2 days	PM + Dev	✅ Done
Define functional requirements	2 days	PM	✅ Done
Technology stack selection	1 day	Tech Lead	✅ Done
Create dataflow diagrams	1 day	Developer	✅ Done

Phase 3: Design (Week 2-3) COMPLETE

Task	Duration	Owner	Status
Problem-solution fit analysis	2 days	PM	✅ Done
System architecture design	2 days	Tech Lead	✅ Done
Database schema design	2 days	Developer	✅ Done
UI/UX wireframes	3 days	Designer	✅ Done
API endpoint design	1 day	Developer	✅ Done

Phase 4: Development (Week 3-6) IN PROGRESS

Sprint 1: Backend Foundation (Week 3-4)

Task	Duration	Owner	Status
MongoDB setup and configuration	1 day	DevOps	⏳ Pending
Create database schemas (Mongoose)	2 days	Backend Dev	⏳ Pending
Express server setup	1 day	Backend Dev	⏳ Pending
Authentication APIs (register/login)	3 days	Backend Dev	⏳ Pending
User management APIs	2 days	Backend Dev	⏳ Pending
bcrypt password encryption	1 day	Backend Dev	⏳ Pending

Sprint 2: Core Features (Week 4-5)

Task	Duration	Owner	Status
Flight management APIs	3 days	Backend Dev	⏳ Pending
Booking system APIs	4 days	Backend Dev	⏳ Pending
React app setup	1 day	Frontend Dev	⏳ Pending
Create reusable components	2 days	Frontend Dev	⏳ Pending
Landing page development	2 days	Frontend Dev	⏳ Pending
Search functionality	2 days	Frontend Dev	⏳ Pending

Sprint 3: Integration (Week 5-6)

Task	Duration	Owner	Status
Frontend-backend integration	2 days	Full-Stack Dev	⏳ Pending
Booking flow implementation	3 days	Full-Stack Dev	⏳ Pending
Customer dashboard	2 days	Frontend Dev	⏳ Pending
Operator dashboard	2 days	Frontend Dev	⏳ Pending
Admin panel	2 days	Frontend Dev	⏳ Pending
Date validation implementation	1 day	Frontend Dev	⏳ Pending

Phase 5: Testing (Week 6-7) PLANNED

Task	Duration	Owner	Status
Unit testing (components & APIs)	2 days	QA + Dev	⏳ Pending

Integration testing	2 days	QA	⏳ Pending
User acceptance testing	2 days	QA + Users	⏳ Pending
Performance testing	1 day	QA	⏳ Pending
Security testing	1 day	Security Team	⏳ Pending
Bug fixing	2 days	Dev Team	⏳ Pending

Phase 6: Deployment (Week 7) PLANNED

Task	Duration	Owner	Status
Production environment setup	1 day	DevOps	⏳ Pending
Database migration	1 day	DevOps	⏳ Pending
Application deployment	1 day	DevOps	⏳ Pending
Monitoring setup	1 day	DevOps	⏳ Pending
Documentation finalization	1 day	PM + Team	⏳ Pending

4. Resource Allocation

Role	Name	Allocation	Responsibilities
Project Manager	[Name]	100%	Planning, coordination, stakeholder management
Full-Stack Developer 1	[Name]	100%	Backend APIs, database, integration
Full-Stack Developer 2	[Name]	100%	Frontend components, UI implementation
UI/UX Designer	[Name]	50%	Wireframes, design, user experience
QA Tester	[Name]	100%	Testing, quality assurance, bug reporting
DevOps Engineer	[Name]	25%	Infrastructure, deployment, monitoring

5. Milestones & Deliverables

Week	Milestone	Deliverables
Week 1	Requirements Complete	Problem statement, Empathy map, User stories, Requirements doc
Week 2	Design Complete	Architecture diagram, Database schema, Wireframes
Week 4	Backend Complete	All APIs functional, Database operational
Week 5	Frontend Complete	All pages developed, Components ready
Week 6	Integration Complete	Fully functional application
Week 7	Launch Ready	Tested, deployed, live application

6. Risk Management

Risk	Probability	Impact	Mitigation Strategy
Timeline delays	Medium	High	Buffer time in schedule, daily standups, agile sprints
Technical challenges	Medium	High	Use proven MERN stack, code reviews, pair programming
Scope creep	High	High	Clear requirements, change control process, MVP focus
Security vulnerabilities	Low	Critical	bcrypt encryption, security audits, HTTPS, best practices
Resource unavailability	Low	Medium	Cross-training, documentation, backup resources

7. Success Metrics

Metric	Target
Project completion on time	100% (Week 7)
Budget adherence	Within 10% of budget
Feature completion	100% of MVP features
Code quality	Zero critical bugs
Performance	< 2 second page load
User satisfaction	4.5/5 stars
System uptime	99%+

© 2026 SB FlightConnect - Project Planning Template

This document is confidential and proprietary
